

Agenda



1 Project Scope

2 Project Execution Methodology

3 Project Schedule

4 Discovery Workshop Schedule

5 Project Monitoring & Control

- Tools & Tracking
- Project Governance
- Project Team



Project Scope




PROCESS	SCOPE	KEY CONSIDERATIONS	Phase
Conga (Apttus)	✓ Conga will be configured to create products and pricing for the Metrio products. ✓ Conga will be configured to provide Customer users with the ability to generate quote documents and MSA (contracts) for the newly configured Metrio products. ✓ New legal entity will be setup in Conga (Apttus) to aid quote creation and contracts for the Metrio products	▪ Conga (Apttus) will be configured basis requirements for	Phase 1
Lead Management	✓ Process Mapping of new leads flow in Salesforce from Metrio ✓ Record Types, Page Layouts and visibility setup ✓ Validation, Assignments, Auto Response	▪ Lead conversion process mapping	Phase 2
Account Management	✓ The existing Account object in the Customer Org will be updated with new fields, page layouts as required to accommodate the relevant Metrio data attributes and business process	▪ Is Account Hierarchy, Account Teams setup required?	Phase 2
Contact Management	✓ The existing Contact object in the Customer Org will be updated with new fields, layouts as required to accommodate the relevant Metrio data attributes and business process	▪ Person Account required?	Phase 2

Project Scope



PROCESS	SCOPE	KEY CONSIDERATIONS	Phase
Opportunity Management	- The existing Opportunity object in the Customer Org will be updated with new fields, layouts as required to accommodate the relevant Metrio data attributes and business process ✓ Record Types, Page Layouts and visibility setup ✓ Validation, Assignments, Auto Response ✓ Approval Process	Opportunity Team, Opportunity Splits, Forecasting not considered.	Phase 2
Products & Pricebook	- Product formatting and process mapping - Pricebook setup - Opportunity Product mapping with Pricebook		Phase 2
Multi Language	In the existing Customer Salesforce Org, French language will be added to the existing multilingual capability, to accommodate the Metrio users		Phase 2
Data Migration(ETL)	- Users - Products - Contacts - Opportunity - Line Items - Files - Activities - Agreement	Only Product migration is there in Phase 1	- Phase 1 - Phase 2

Project Execution Methodology

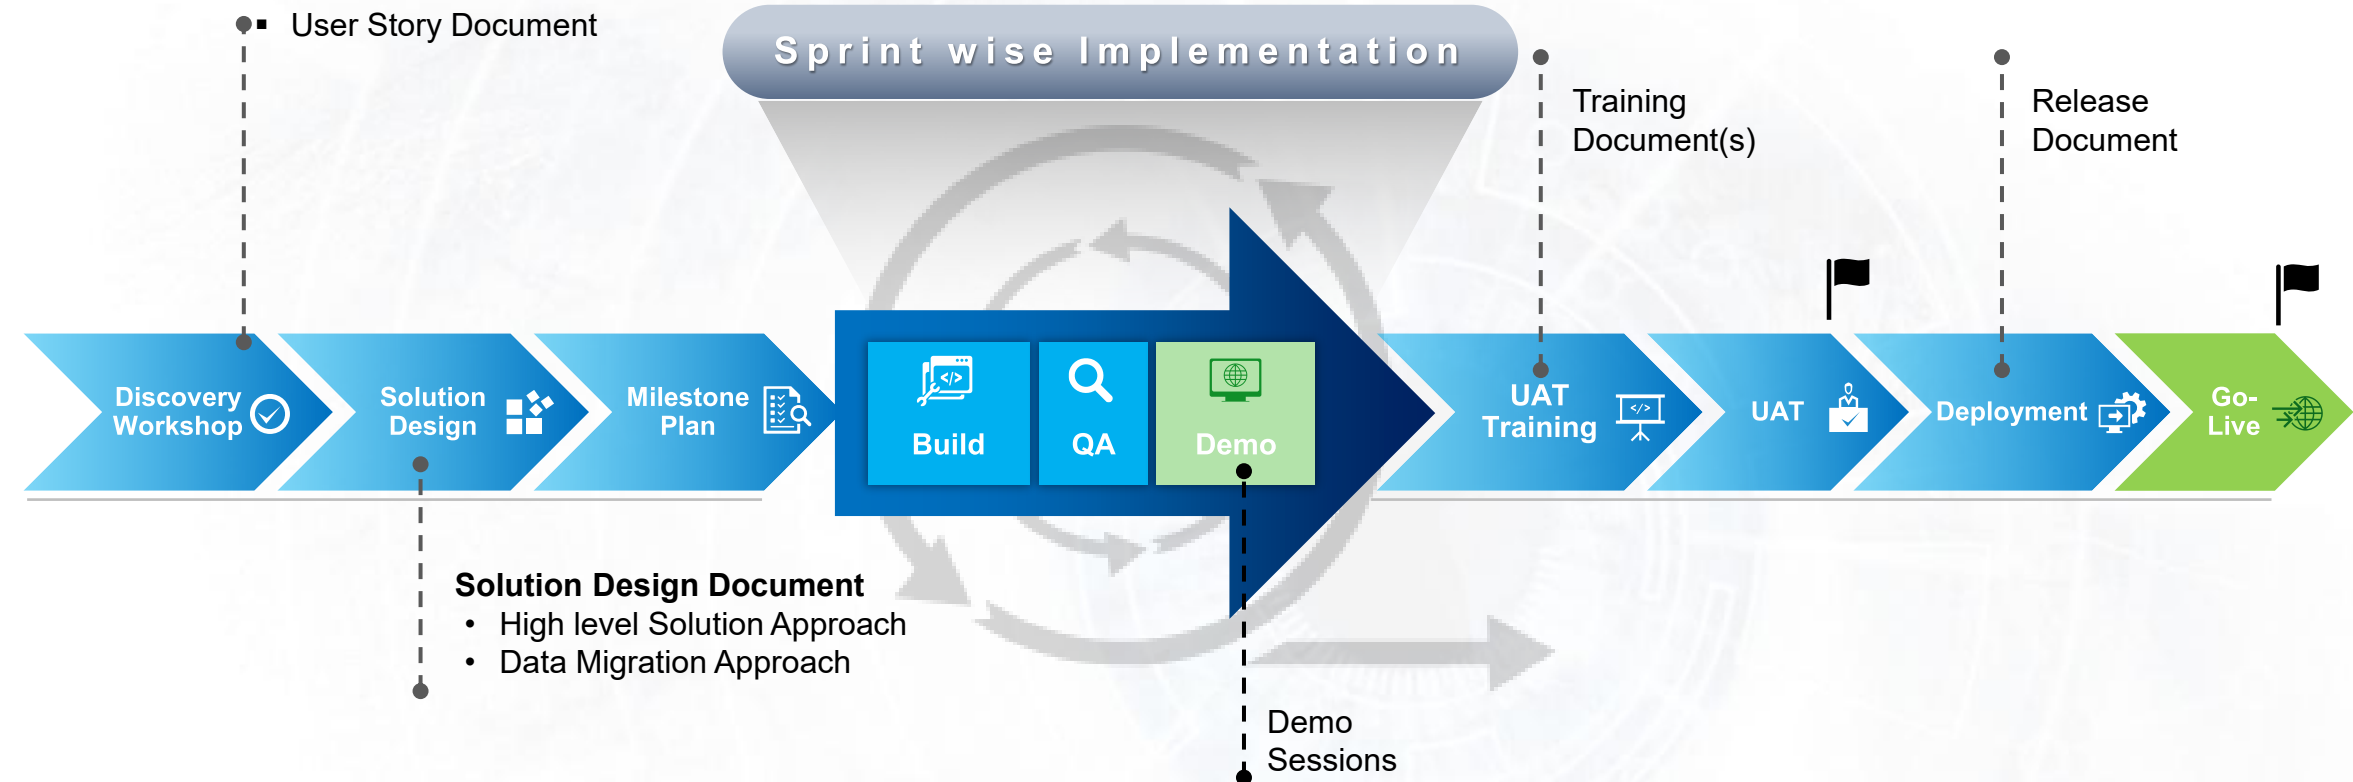

User Story
Documentation



Sessions with
Business
users



Business
Process Maps



Product
Backlog

Project Schedule



With the given set of requirements, Company proposes the below timeline for execution of this project

Phase 1	16-Aug WK1	22-Aug WK2	29-Aug WK3	5-Sep WK4	12-Sep WK5	19-Sep WK6	26-Sep WK7	3-Oct WK8	10-Oct WK9	17-Oct WK10	24-Oct WK11	31-Oct WK12	7-Nov WK13
Discovery													
KT on Product Configuration													
Design & Impact Analysis													
Build (App + Data) Iteration 1													
Test Iteration 1													
Build (App + Data) Iteration 2													
Test Iteration 2													
Build (App + Data) Iteration 2													
Test Iteration 2													
SIT													
TTT													
UAT													
Prod Movement													

PHASE 1	
SDLC	Timeline
KT on Product Configuration	Aug 16 – Aug 26
Build & Test iteration	Aug 29 - Oct 7
UAT	Oct 24 – Nov 4
Prod Movement	Nov 7 – Nov 9

Phase 2	24-Oct WK11	31-Oct WK12	7-Nov WK13	14-Nov WK14	21-Nov WK15	28-Nov WK16	5-Dec WK17	12-Dec WK18	19-Dec WK19	26-Dec WK20	2-Jan WK21	9-Jan WK22	16-Jan WK23	23-Jan WK24	30-Jan WK25	6-Feb WK26	13-Feb WK27	20-Feb WK28	27-Feb WK29
Build (App + Data) Iteration 1																			
Test Iteration 1																			
Build (App + Data) Iteration 2																			
Test Iteration 2																			
Build (App + Data) Iteration 3																			
Test Iteration 3																			
Build (App + Data) Iteration 4																			
Test Iteration 4																			
SIT																			
TTT																			
Regression Testing																			
End-to-End UAT																			
Prod Migration																			
Hypercare																			

PHASE 2	
SDLC	Timeline
Discovery	Sep 12 – Oct 21
Design and Impact Analysis	Sep 12 – Oct 21
Build & Test iteration	Oct 24 – Dec 23
SIT	Dec 26 – Jan 6
Regression Testing	Jan 9 – Jan 20
End to End UAT	Jan 23 – Feb 10
Prod Movement	Feb 13 – Feb 17
Hypercare	Feb 20 – Mar 3

Project Monitoring & Control: Tools & Tracking



#	Activity	Tool/ Tracking Mechanism
1	Project Schedule	MS Excel
2	Project Tasks, Activities, Assignments & Defect Tracking	JIRA
3	Project Source Code Control & Versioning	TBD
4	Risks, Actions, Issues, Dependencies	MS Excel
5	Project Status Reporting	Email/MS PPT
6	Project Governance Reporting	MS PPT
7	In-process Project Document Mgmt	Sharepoint
8	QA Artefacts (Test Plans, Scenarios, Test Cases)	Sharepoint
9	Team Collaboration Tool	MS Teams

Project Governance



Meeting	Frequency	Attendees	Agenda	Finalized Day/Time
Stand-up Meeting	Daily	Company Project Team	Daily Status & Progress will be reviewed	
Weekly Status Meeting	Weekly	Client & Company	Project Status, Risks, Issues, Dependencies & Action Items	Every Monday 8:30AM EST 30 mins??
Weekly Status Report	Weekly	To be sent to Client by PM	Project Status, Risks, Issues, Dependencies & Action Items	Before WSM

THANK YOU
