



Process & Data Migration

Monthly Governance Call

Presented to: _____


Agenda



- **Project Team**
- **Project Schedule & Plan**
- **Overall Health Review**
- **Risks & Mitigation Actions**
- **Hits / Misses**
- **JIRA Stories & Record Migration Status**
- **Financial Burndown**

Project Schedule & Plan

As of Today

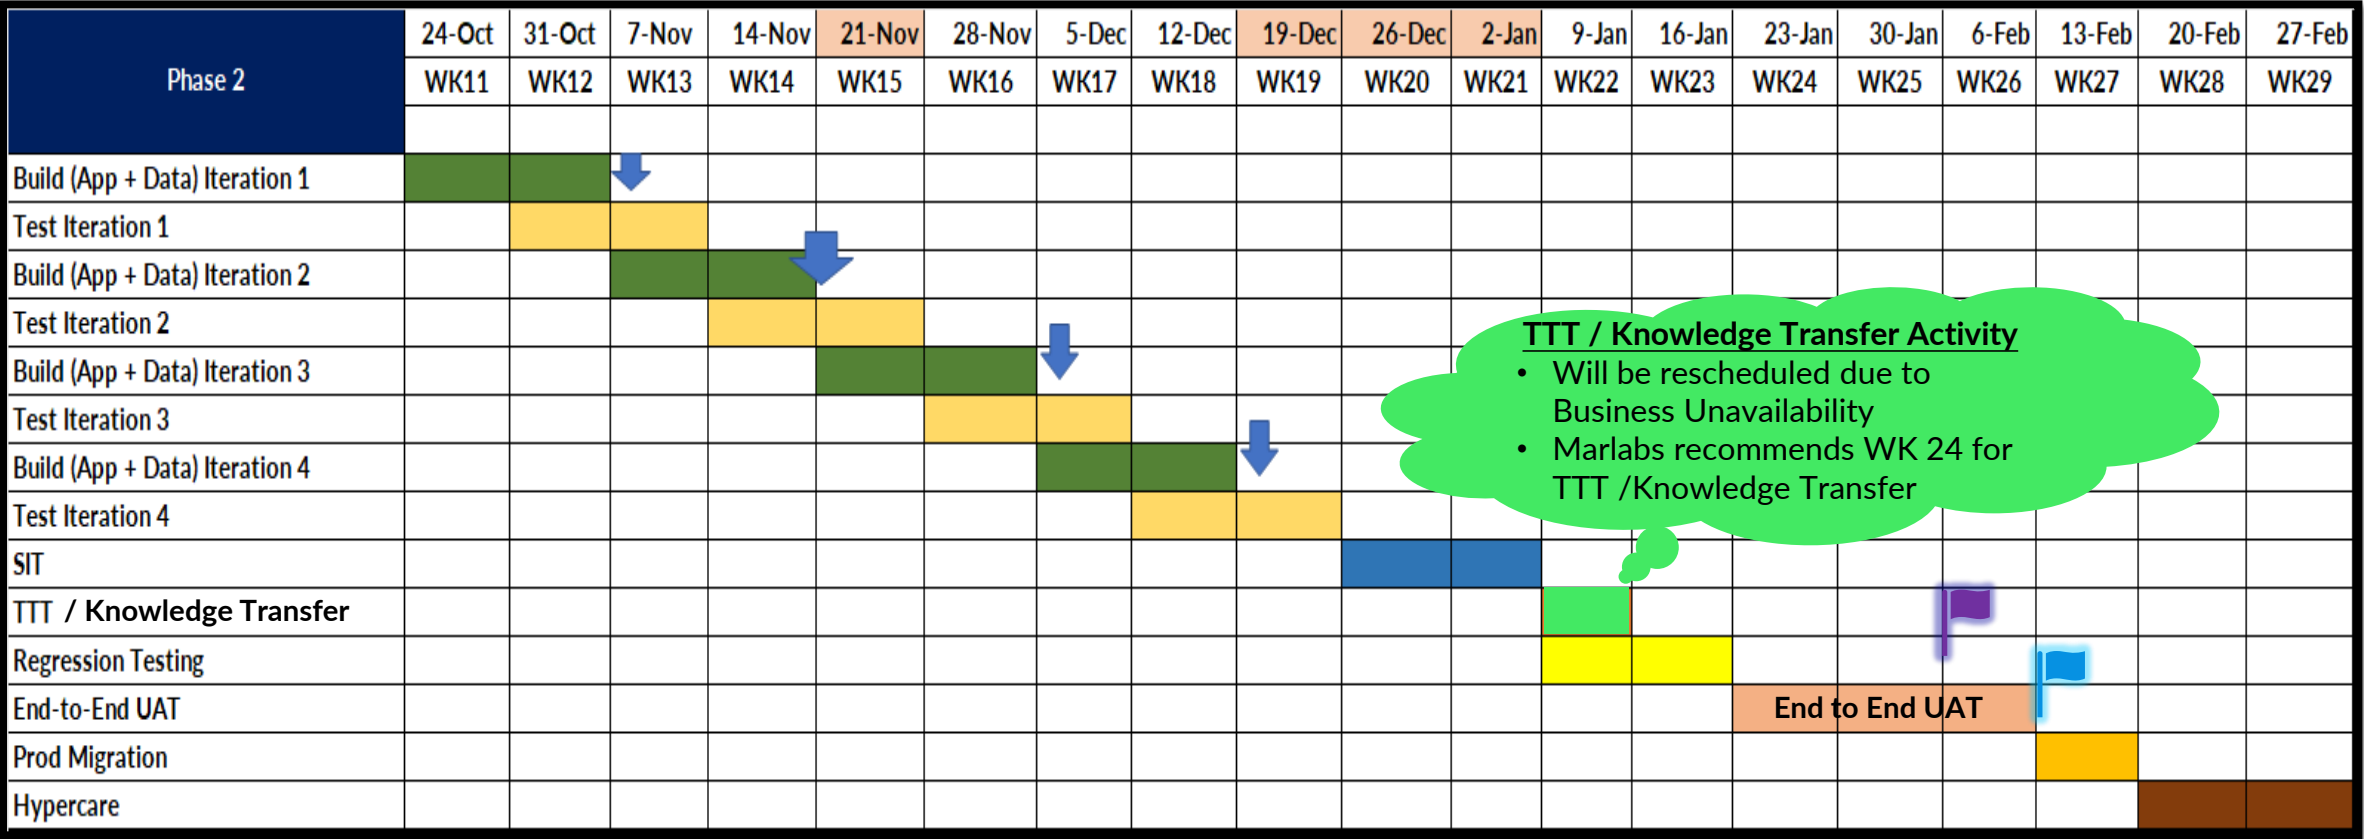

TTT / Knowledge Transfer Activity

- Will be rescheduled due to Business Unavailability
- Marlabs recommends WK 24 for TTT /Knowledge Transfer



UAT Sign Off – Go No Go Decision – 10th Feb 2023



Cutover plan / Go live Plan – 3rd Feb 2023

Cut-Over / Go Live Plan

Need scheduled meetings with Amy’s team / SME’s deployment team while our team prepares the plan

Planned (Phase II)

Technical Go Live Date: Feb 18th, 2023
Hypercare: Feb 20th, 2023 onwards

Upcoming Holidays

Jan 16th, 2023 – Martin Luther King Holiday
Jan 26th, 2023 – Republic Day (India)

Overall Health Review



Phase 1 16th
Aug – 16th
Nov 2022

Requirement
Gathering
16th – 25th Nov

Regression 9th - 20th
Jan 2023

Production
Movement
13th Feb – 17th Feb

Phase II –
Initiated
16th Nov
2022

Construct & Test
Iteration
21st Nov – 6th Jan
2023


We are here

UAT
23rd Jan – 10th Feb.

Hyper Care
20th Feb – 3rd March

Phase I – Completed with all Deliverables on Time.

Duration : 16th Aug 2022 – 15th Nov 2022

Milestone	Status
SO Template Modification for Metrio Products	Completed
Product Catalogue Migration	Completed
Price book Catalogue Migration	Completed
Production Migration (Technical Go Live)	Completed

Phase II (Sprint 53) – InProgress and On Schedule

Duration : 16th Nov 2022 – 3rd Feb 2023

Milestone	Planned End Date	Actual date	Status
Asset Migration POC	5 th Jan	5 th Jan	Completed
Engagement/ Activities Migration POC	3 rd Jan	2 nd Jan	Completed
File & Folder Migration	5 th Jan	5 th Jan	Completed
Migration for Contact	13 th Jan	12 th Jan	Completed
Migration of Leads/Opportunity	13 th Jan	TBD *	In Progress
Migration of Accounts	13 th Jan	TBD *	In Progress
Strategy Documentation & FDD	23 rd Dec	TBD*	In progress
Regression Testing	20 th Jan		In Progress
UAT	10 th Feb		Not Initiated
Production/Migration	17 th Feb		Not Initiated
Hyper Care	3 rd March		Not Initiated

TBD * - Awaiting Business Inputs. Once we have the inputs it may take max two days to complete

Risks & Mitigation Actions

Phase I

#	Risk	Mitigation Action	Status
1	Project schedule delay because of delay of selecting of Data Migration Tools.	Marlabs immediately deployed resources to achieve migrating the POC's on Talend (70%) and Tableau (30%) in a very short duration	Completed
2	Recurring SO Template Issue causing Issue in Phase I production migration activity.	The whole Issue was closed after the segments was recreated again. Raised a concern with Apttus Conga Team.	Completed

Phase II

#	Risk	Mitigation Action	Status
1	Planned activities hampered due to delays in Sandbox refresh activities	Team worked on weekends to mitigate the delay in planned activities and bring it on schedule	In Progress
2	Delay in Mapping Sheet Sign Off	UAT migration Initiated based on conditional Sign Off. Business Inputs required on get a Sign Off by Jan 18 th EOD EST to avoid impact on Schedule.	In Progress
3	Schedule delay due to business inputs	Marlabs expects business inputs to be provided by Jan 18 th EOD EST to avoid any Impact to schedule	In Progress

Hits/Misses

What went Well ?

- **EARLY DECISION ON FINALIZING MIGRATION TOOLS & APPROACH.**
- **PHASE 2 (15%) WORK COMPLETED DURING PHASE 1 CONSTRUCT.**
- **ADDITIONAL QA SUPPORT LOOPED IN ON TIME IN PHASE 2**
- **TEAM PROVIDED ADDITIONAL SUPPORT ON TWO JIRA STORIES (NON METRIO ENGAGEMENT)**
- **GOOD TEAM COORDINATION (NASDAQ INDIA, METRIO, HUBSPOT & MARKETO)**

What can be Improved ?

- **JIRA UPDATES COULD HAVE BEEN STREAMLINED**
- **BURN DOWN DETAILS WAS NOT AT PAR WITH NASDAQ EXPECTATIONS**

JIRA Stories & Record Migration Status

Phase 1 Stories - Status	Σ of Stories	Σ of Stories Points
Verified / Closed	18	46
Total	18	46

Phase 2 Stories - Status	Σ of Stories	Σ of Stories Points	ETA	Comments
Verified / Closed	17	NA	NA	
Under Verification (QA)	9	NA	18 th Jan	
Under Verification (QA) & Blocked	3	NA	20 th Jan	Need clarifications from Business by 18 th Jan EOD (EST)
Total	29	88		



Phase II -Records Migration – Status (to UAT environment)

Total Records Count	103,428
Successfully Migrated records Count	102,531 (99.13%)
Errored Records Count	896 (0.87%)
Total Entity Count	12

Financial Burndown

Current Budget Data (As of 8 th Jan)	
A. Total Budget	\$ 251,304
B. Consumed / Invoiced	\$ 155,823
C. Pending (TS to be submitted / approved)	\$ 7,744
D. Remaining Budget = (A - B - C)	\$ 87,737

Estimated Budget Data (from 9 th Jan to 3 rd Mar 2023) for 8 Resources + PM	
D. Remaining Budget (as of 8 th Jan)	\$ 87,737
E. Estimated consumption for 9 th Jan to 31 st Jan	\$ 34,086
F. Estimated consumption for 1 st Feb to 3 rd Mar	\$ 49,155
G. Estimated Remaining Budget (End of project) = (D - E - F)	\$ 4,496

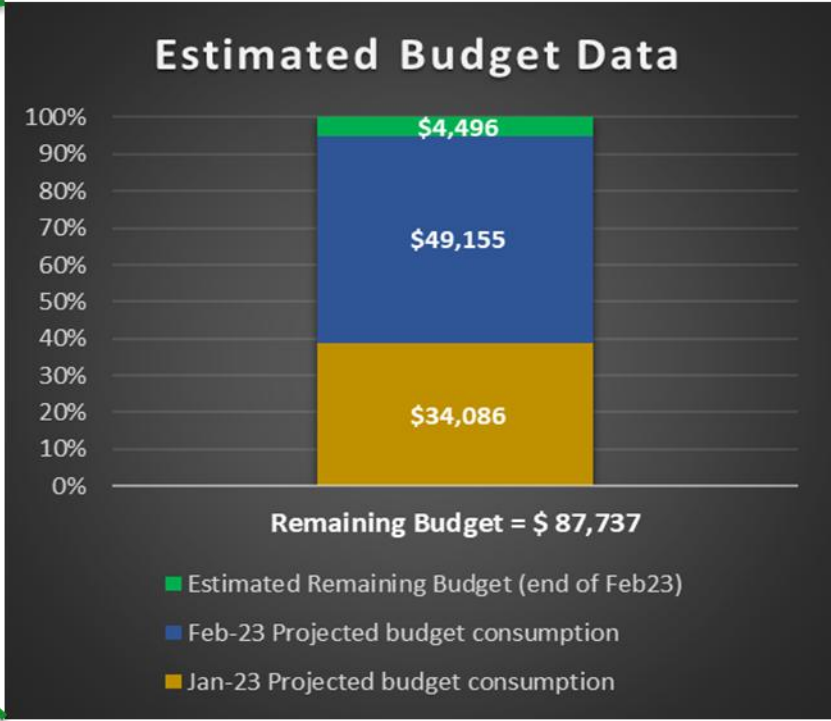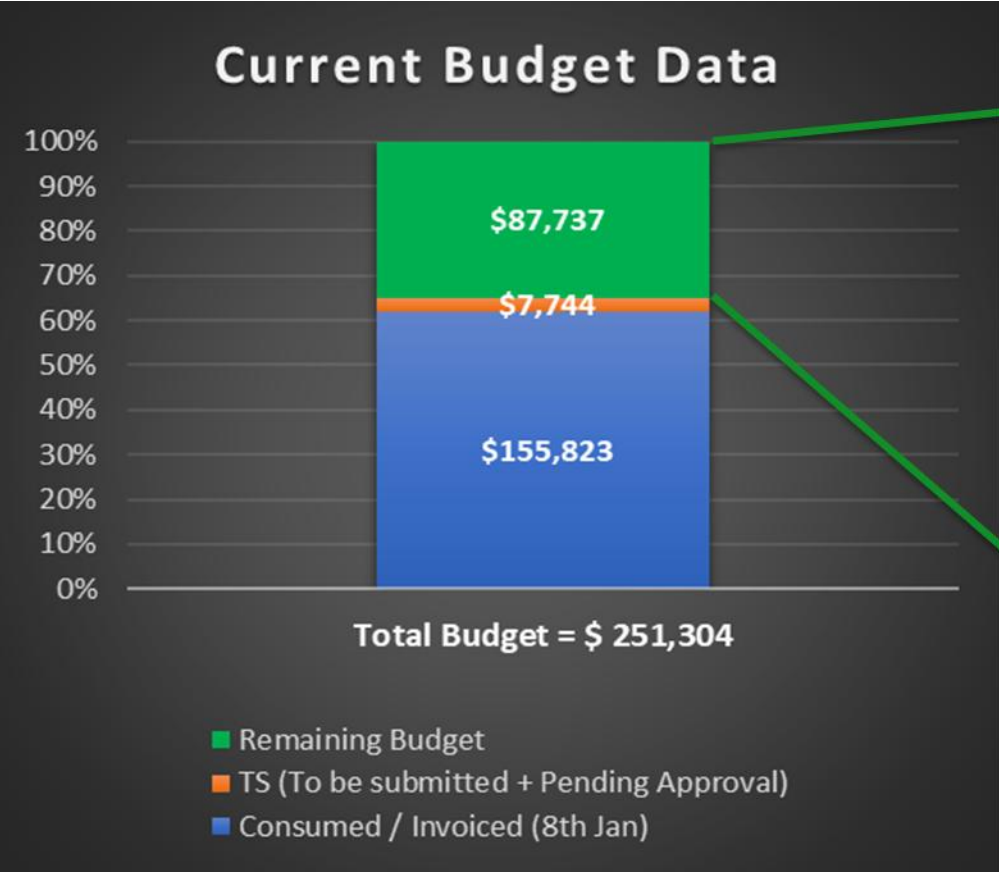



THANK YOU
